

ENVIRONMENTAL MANAGEMENT PROGRAMME

for


DWARSWEGSTRAND HOLIDAY RESORT

on

Erf 720, Mossel Bay Municipality

In terms of the

National Environmental Management Act (Act No. 107 of
1998, as amended) & 2014 Environmental Impact
Regulations (as amended)

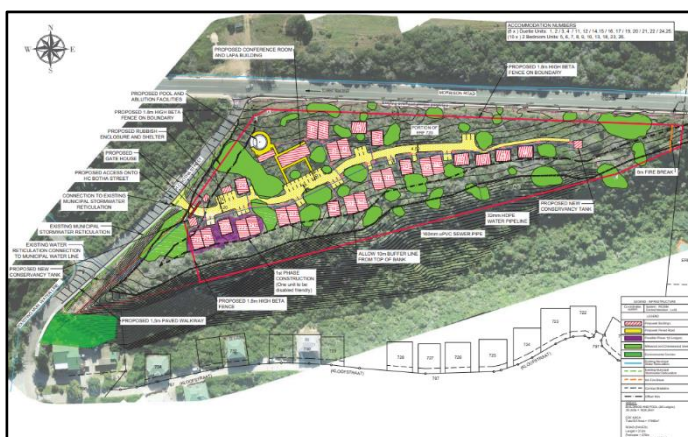

Prepared for Applicant: Kaapland Onderwys Trust (KOT)

Date: 22 August 2023

Author of Report: Ms Louise-Mari van Zyl

Author Email: louise@cape-eaprac.co.za

Report Reference: MOS643/08

Department Reference: 16/3/3/6/7/1/D6/17/0045/23

Case Officer: Steve Kleinhans

Cape EA Prac

Cape Environmental Assessment Practitioners

Tel: +27 44 874 0365 PO Box 2070, George 6530
Fax: +27 44 874 0432 17 Progress Street, George

www.cape-eaprac.co.za



DOCUMENT TRACKING**DOCUMENT HISTORY**

DOC REF	REVISION	DATE	AUTHOR
MOS643/08	Draft EMPPr	2023-08-22	Ms Louise-Mari van Zyl

APPROVAL FOR RELEASE

NAME	TITLE	SIGNATURE
Ms Louise-Mari van Zyl	Ms	

DISTRIBUTION FINAL

DESIGNATION	NAME	EMAIL / FAX
Potential Stakeholders	Stakeholder Register	Preferred Communication
Mossel Bay Municipal Office	Mr Carel Venter	Electronic Submission
DEA&DP, George	Steve Kleinhans & Admin Registry	Electronic Submission

APPOINTED ENVIRONMENTAL ASSESSMENT PRACTITIONER:**Cape EAPrac Environmental Assessment Practitioners****PO Box 2070****George****6530****Tel: 044-874 0365****Fax: 044-874 0432**

Report written & compiled by: **Louise-Mari van Zyl** (MA Geography & Environmental Science) who has over 20 years' experience as an environmental practitioner. Registered Environmental Assessment Practitioner with the Environmental Assessment Practitioners of South Africa, EAPSA, **Registration Number 2019/1444.**

Registrations: Director **Louise-Mari van Zyl** (MA Geography & Environmental Science [US]; Registered Environmental Assessment Practitioner with the Environmental Assessment Practitioners of South Africa, EAPSA, **Registration Number 2019/1444.** Ms van Zyl has over twenty years' experience as an environmental practitioner.

PURPOSE OF THIS REPORT:

Environmental Management Programme

APPLICANT:

Kaapland Onderwys Trust (KOT)

CAPE EAPRAC REFERENCE NO:

MOS643/08

SUBMISSION DATE

22 August 2023

ENVIRONMENTAL MANAGEMENT PROGRAMME

for

DWARSWEGSTRAND HOLIDAY RESORT

on

Erf 720, Mossel Bay Municipality

In terms of the

National Environmental Management Act (Act No. 107 of 1998, as amended) & 2014
Environmental Impact Regulations (as amended)

Submitted for:

Stakeholder Review & Comment

- This report is the property of the Author/Company, who may publish it, in whole, provided that:
- Written approval is obtained from the Author and that *Cape EAPrac* is acknowledged in the publication;
- *Cape EAPrac* is indemnified against any claim for damages that may result from any publication of specifications, recommendations or statements that is not administered or controlled by *Cape EAPrac*;
- The contents of this report, including specialist/consultant reports, may not be used for purposes of sale or publicity or advertisement without the prior written approval of *Cape EAPrac*;
- *Cape EAPrac* accepts no responsibility by the Applicant/Client for failure to follow or comply with the recommended programme, specifications or recommendations contained in this report;
- *Cape EAPrac* accepts no responsibility for deviation or non-compliance of any specifications or recommendations made by specialists or consultants whose input/reports are used to inform this report; and
- All figures, plates and diagrams are copyrighted and may not be reproduced by any means, in any form, in part or whole without prior written approved from *Cape EAPrac*.

Report Issued by:

Cape Environmental Assessment Practitioners

Tel: 044 874 0365

Fax: 044 874 0432

Web: www.cape-eaprac.co.za

PO Box 2070

17 Progress Street

George 6530

ORDER OF REPORT

Environmental Management Plan

- Appendix 1 : Locality Plans
- Appendix 2 : Site Plans
- Appendix 3 : Environmental Guidelines for construction
- Appendix 4 : EAP Company Profile
- Appendix 5 : Environmental Authorisation (Pending)

TABLE OF CONTENTS

1. INTRODUCTION	1
1.1 Purpose of the EMPr.....	3
1.2 Status of the EMPr.....	3
2 EMPR PHASING	4
2.1 Pre-Construction Phase	4
2.2 Construction Phase.....	4
2.3 Operational / maintenance Phase	4
2.4 Closure and Decommissioning Phase.....	4
3 LEGISLATIVE REQUIREMENTS.....	5
3.1 National Environmental Management Act (NEMA, Act 107 of 1998)	5
3.2 Environment Conservation Act, 1989 (ECA)	5
3.3 National Environmental Management: Biodiversity Act (NEM:BA) (Act 10 of 2004)	5
3.4 National Waste Management Strategy	6
3.5 National Water Act (NWA, Act 36 of 1998).....	6
3.6 National Forest Act (Act 84 of 1998)	6
3.7 National Heritage Resources Act (Act 25 of 1999)	7
3.8 Occupational Health and Safety act (Act 85 of 1993)	7
4 ENVIRONMENTAL IMPACTS & MITIGATIONS	8
4.1 Mitigations.....	8
5 RESPONSIBILITIES	9
5.1 Holder of the EA	10
5.2 Engineers AND Contractors.....	10
5.3 Ecological Control Officer (ECO).....	11
5.4 ECO Site Visit Frequency	12
5.5 Environmental Induction & Training	12
6 PRE-CONSTRUCTION DESIGN CONSIDERATIONS	13
6.1 Stormwater Management Preparation.....	13
6.2 gabion design	Error! Bookmark not defined.
7 CONSTRUCTION CONSIDERATIONS.....	19
7.6 STOCKPILE management.....	24
7.8 Minimising Erosion.....	27
7.9 Rehabilitation & Botanical Management.....	28
7.10 Fauna Management.....	29
7.13 Health and Safety	32
8 OPERATIONAL/MAINTENANCE PHASE ENVIRONMENTAL MANAGEMENT REQUIREMENTS.....	33

8.1	Stormwater Management.....	33
8.2	Botanical / Landscaping / rehabilitation	33
9	MONITORING, MAINTENANCE & VALIDTY OF EMPR.....	35
9.1	MONITORING	35
9.2	POST- CONSTRUCTION MAINTENANCE & VALIDTY OF EMPR.....	Error!
	Bookmark not defined.	
9.3	Monitoring Timeframes Summary	35
9.4	Environmental Audits	35
9.5	Audit Reports Frequencies and Format.....	35
10	DECOMMISSIONING PHASE ENVIRONMENTAL MANAGEMENT REQUIREMENTS ..	38
11	NON-COMPLIANCE	38
11.1	Procedures	39
12	REFERENCES	40

FIGURES

Figure 1:	Locality map of Erf 720 (yellow outlined area) (CapeFarmMapper, 2023).	2
Figure 2:	Proposed development footprint on a portion of Erf 720 (red outlined area) (CapeFarmMapper, 2023).....	2
Figure 3:	Responsibilities.	10

TABLES

Table 1:	Checklist in terms of Appendix 4 of Regulation 982 of 2014 EIA Regulations.....	vii
Table 2:	List of Mitigation Measures & Associated Management Requirements.....	8
Table 3:	Site Clearance Methodology.	19
Table 4:	Monitoring Timeframe Summary	35
Table 5:	Audit Reports Timeframe Summary	36
Table 6:	Environmental Audit Requirements	36

ENVIRONMENTAL MANAGEMENT PROGRAMME REQUIREMENTS

Appendix 4 of Regulation 982 of the 2014 EIA Regulations contains the required contents of an Environmental Management Programme (EMPr). The checklist below serves as a summary of how these requirements were incorporated into this EMPr.

Table 1: Checklist in terms of Appendix 4 of Regulation 982 of 2014 EIA Regulations

Requirement	Description
Details and expertise of the EAP who prepared the EMPr; including curriculum vitae.	Ms Louise-Mari van Zyl for Cape Environmental Assessment Practitioners. See Appendix 4.
A detailed description of the aspects of the activity that are covered by the EMPr as identified by the project description.	<u>Section 1</u>
A map at an appropriate scale which superimposes the proposed activity, its associated structures, and infrastructure on the environmental sensitivities of the preferred site, indicating any areas that must be avoided, including buffers	Appendix 1
A description of the impact management objectives, including management statements, identifying the impacts and risks that need to be avoided, managed and mitigated as identified through the environmental impact assessment process for all the phases of the development including – (i) Planning and design; (ii) Pre-construction activities; (iii) Construction activities; (iv) Rehabilitation of the environment after construction and where applicable post closure; and (v) Where relevant, operation activities.	<u>Section 4</u> – Environmental Impacts & Mitigations <u>Section 5</u> - Responsibilities <u>Section 6</u> – Pre-Construction Design <u>Section 7</u> – Construction Phase <u>Section 8</u> – Operation Phase
A description and identification of impact management outcomes required for the aspects contemplated above.	<u>Section 4</u>
A description of the proposed impact management actions, identifying the manner in which the impact management objectives and outcomes contemplated above will be achieved and must, where applicable include actions to – (i) Avoid, modify, remedy control or stop any action, activity or process which causes pollution or environmental degradation; (ii) Comply with any prescribed environmental management standards or practises; (iii) Comply with any applicable provisions of the Act regarding closure, where applicable; and (iv) Comply with any provisions of the Act regarding financial provisions for rehabilitation, where applicable.	<u>Section 4</u> <u>Section 6</u> <u>Section 7</u> <u>Section 8</u>
The method of monitoring the implementation of the impact management actions contemplated above.	<u>Section 9</u> <u>Section 11</u>
The frequency of monitoring the implementation of the impact management actions contemplated above.	<u>Section 9</u>

Requirement	Description
An indication of the persons who will be responsible for the implementation of the impact management actions.	<u>Section 5</u>
The time periods within which the impact management actions must be implemented.	Not Applicable
The mechanism for monitoring compliance with the impact management actions.	<u>Section 9</u>
A program for reporting on compliance, taking into account the requirements as prescribed in the Regulations.	<u>Section 9</u>
<p>An environmental awareness plan describing the manner in which –</p> <p>(i) The applicant intends to inform his or her employees of any environmental risk which may result from their work; and</p> <p>(ii) Risks must be dealt with in order to avoid pollution or the degradation of the environment.</p>	<u>Section 5</u> <u>Section 6</u> <u>Section 7</u> <u>Section 8</u> <u>Section 9</u>
Any specific information that may be required by the competent authority.	Not Applicable.

ABBREVIATIONS AND ACRONYMS

BSP	Biodiversity Sector Plan - to inform land use planning, environmental assessments, land and water use authorisations, as well as natural resource management, undertaken by a range of sectors whose policies and decisions impact on biodiversity.
CARA	Conservation of Agricultural Resources Act (Act 43 of 1983) - provides for control over the utilization of the natural agricultural resources of the Republic in order to promote the conservation of the soil, the water sources and the vegetation and the combating of weeds and invader plants; and for matters connected therewith.
CBA	Critical Biodiversity Area - areas required to meet biodiversity targets for ecosystems, species and ecological processes, as identified in a systematic biodiversity plan.
DFFE	National Department of Forestry, Fisheries & the Environment – the national authority responsible for the sustainable environmental management and integrated planning.
DEA&DP	Department of Environmental Affairs and Development Planning – the provincial authority for sustainable environmental management and integrated development planning. The competent authority is this case.
DWS	Department of Water & Sanitation Affairs – National authority mandated to enforce the National Water Act (NWA).
EA	Environmental Authorisation – Authorisation obtained on completion of an Environmental Impact Assessment in terms of the National Environmental Management Act (NEMA).
ECA	Environment Conservation Act, 1989 - To provide for the effective protection and controlled utilization of the environment and for matters incidental thereto.
ECO	Ecological Control Officer – independent site agent appointed to observe and enforce the implementation of environmental policies and principles on a development site.
EIA	Environmental Impact Assessment - a process of evaluating the likely environmental impacts of a proposed project or development, taking into account inter-related socio-economic, cultural and human-health impacts, both beneficial and adverse.
EMPr	Environmental Management Programme – an environmental management tool used to ensure that undue or reasonably avoidable adverse impacts of the construction, operation and decommissioning of a project are prevented and that positive benefits of the projects are enhanced.
GIS	Geographic Information System - system designed to capture, store, manipulate, analyse, manage, and present all types of geographical data.
GPS	Global Positioning System - a radio navigation system that allows land, sea, and airborne users to determine their exact location, velocity, and time 24 hours a day, in all weather conditions, anywhere in the world.
NEMA	National Environmental Management Act (Act 107 of 1998, as amended) – national legislation that provides principles for decision-making on matters that affect the environment.

- NEM:BA** National Environmental Management: Biodiversity Act (Act No.10 of 2004) – provides for the management and conservation of South African biodiversity within the framework of NEMA.
- NFA** National Forestry Act (Act No.84 of 1998) - provides for the protection of forests, as well as specific tree species within South Africa.
- NSBA** National Spatial Biodiversity Assessment – aims to assess the state of South Africa’s biodiversity based on best available science, with a view to understanding trends over time and informing policy and decision-making across a range of sectors.
- NWA** National Water Act (Act No.36 of 1998) - ensures that South Africa's water resources are protected, used and managed.

1. INTRODUCTION

Cape Environmental Assessment Practitioners (Cape EAPrac) was appointed by the Applicant, Kaapland Onderwys Trust (KOT) to develop an Environmental Management Programme (EMPr) which will be used to promote and ensure environmental monitoring and control during all relevant phases (pre-construction, construction, operational as well as maintenance) associated with the proposed activity.

The **Applicant**, intends to develop a Holiday Resort on a portion of Erf 720, Dwarswegstrand (Glentana/Outeniqua), Mossel Bay Municipality. Erf 720 is located between Bothastrand and Outeniqua Strand, on the corner of H.C. Botha Street and Morrison Road.

The proposed development includes the following:

- Eight (8) x Duette holiday units.
- Ten (10) x Two-bedroom holiday units.
- Conference room.
- Lapa building.
- Pool with ablution facilities.
- Entrance gate and gatehouse (entrance from H.C. Botha Street).
- Waste enclosure and shelter.
- Holding/Conservancy tank.
- Internal roads (3.2m – 5.2m wide) and parking areas will be constructed with eco-blocks and topsoil. This will allow grass to grow and be in line with the low impact concept.
- Paved walkway in H.C. Botha Street Road Reserve (1.5m wide and approximately 152m long).
- Fence (1.8m high ClearVu) along existing tarred road boundaries (Morrison Road and H.C. Botha Street). No fencing along the southern boundary of proposed development footprint.

Water supply infrastructure is readily **available** from an existing 110mm uPVC Municipal line along H.C. Botha Street running along the south-western boundary of Erf 720. Water will be distributed throughout the proposed development site using HDPE pipelines ranging in diameters between 63mm and 90mm, depending on the pressure that is available and the flow required. Water pipelines will follow the internal road network.

Municipal **electrical** supply point (11kV) is already **available** for connection and approved by Mossel Bay Municipality in 2020. Due to the low electrical requirement of the proposed development (100kVA), a pole-mounted transformer will be placed on the closest municipal wooden electrical pole structure to the entrance of the proposed development in H.C. Botha Street. A new low voltage supply cable (underground) will be installed from the bottom of the pole-mounted transformer (and metering point), to the entrance of the proposed development, from where the rest of the reticulation to the holiday resort will be facilitated along the internal road network.

An underground **holding/conservancy tank** for **sewage** will be installed in the north-eastern corner of the property, or alternatively near the Entrance Gate. Internal sewer pipelines (160mm uPVC) will link the conservancy tank(s) and resort units, along the internal access roads. Resort units will be connected to the internal sewer line using 110mm uPVC pipes. The internal sewer reticulation network will be designed to gravitate towards the conservancy tank(s). The planning is such that the conservancy tank(s) can be converted to pump stations once municipal bulk sewer services become available on Morrison Road. Until such time as the area has municipal sewage infrastructure, the development will be serviced through the conservancy tanks and either the Municipality or private

tanker suppliers will empty the tanks as and when required and deposit the sewage at the Municipal Sewage Works.

Access to the site is proposed directly off **H.C. Botha Street** and will be provided with an entrance gate for controlled access.

According to Element Engineers a minor percentage (~5%) of **stormwater** drains in a westerly direction towards H.C. Botha Street and will be discharged into the existing municipal stormwater network along the road. The remaining area will allow for stormwater to infiltrate in accordance with SUDS. All internal roads and parking areas will be developed using eco-blocks that have a high level of infiltration resulting in negligible stormwater runoff. Litter traps will be placed at all stormwater outlets (headwalls) with energy dissipation measures and rain water tanks are mandatory for the units. The minimum stormwater pipe diameter is 450mm.



Figure 1: Locality map of Erf 720 (yellow outlined area) (CapeFarmMapper, 2023).



Figure 2: Proposed development footprint on a portion of Erf 720 (red outlined area) (CapeFarmMapper, 2023).

This activity requires an Environmental Authorisation in terms of the National Environmental Management Act (NEMA, Act 107 of 1998) before commencing, as well as for future maintenance and repairs of the structure.

This document provides part of a series of documents that is being circulated for public and stakeholder input as part of the Basic Assessment process, before being provided to the provincial

competent authority, the provincial Department of Environmental Affairs & Development Planning (DEA&DP) for decision making.

This EMPr contains **management requirements** and **recommendations** made by *Cape EAPrac*, the appointed specialist as well as in terms of the regulations contained in the **National Environmental Management Act** (NEMA, Act 107 of 1998) and environmental best practice principles.

This EMPr must be updated to include any conditions of the **Environmental Authorisation** (EA) as issued.

1.1 PURPOSE OF THE EMPR

The purpose of this EMPr is to ensure that the environmental impacts and management of the various phases, of the proposed activity, on the receiving environment are managed, mitigated and kept to a minimum (ie. the **outcome** of implementing the EMPr). The EMPr must provide easily understood and clearly defined **actions** that must be implemented during each phase of the proposed activity. The EMPr is a dynamic document that is flexible and responsive to new and changing circumstances.

The document is binding on the Applicant (Kaapland Onderwys Trust), all contractors and sub-contractors to the site.

It must be included as part of any documents / agreements, as well as contractual documents between the Applicant and any contractors.

Copies of this EMPr must be kept on site and all **senior personnel** are expected to familiarise themselves with the content of this EMPr.

Any changes or deviations to this EMPr must be authorised by the competent authority in the event that any environmental outcomes are amended.

1.2 STATUS OF THE EMPR

It is of utmost importance that this EMPr be read in conjunction with any legally obtained authorisations such as an Environmental Authorisation (EA). This EMPr is viewed as a dynamic document that must be reviewed and updated on a continual basis.

The EMPr is valid for the duration of the project (both for construction as well as future maintenance) with each applicable phase corresponding to the identified requirements.

2 EMPR PHASING

2.1 PRE-CONSTRUCTION PHASE

The pre-construction phase refers to the design phase of the project. This will ensure that any requirements and best practise mechanisms are built into the planning / design phase to be developed in the construction and operational phase. In term of this application, the pre-construction can be considered as the site selection and engineering designs and mitigations.

2.2 CONSTRUCTION PHASE

The construction phase refers to the actual construction of the development on the property, and includes all earthworks and installation of bulk services (water, sewerage, roads, stormwater, electricity etc.). In terms of this application, this phase relates to the construction of the civil engineering services and infrastructure.

2.3 OPERATIONAL / MAINTENANCE PHASE

The Operation Phase of this project relates to the ongoing management and maintenance required to ensure sustainable development. In terms of this application, this refers to all activities that are undertaken once construction is completed and the site is handed over to the Applicant.

All future maintenance of the structure (i.e. after flooding and erosion) must be implemented in accordance with this EMPr (procedures for construction activities to be followed).

The Applicant must ensure that the Operational Phase maintains the underpinning principles 'Duty-of-Care-to-the-Environment' and ideals of sustainable development.

Maintenance of the structure, once installed, must be undertaken in accordance with this management & maintenance plan.

2.4 CLOSURE AND DECOMMISSIONING PHASE

Decommissioning refers to the process of removing the operating assets of any development after completion of the operating life cycle.

The decommissioning phase is not applicable because the proposed activity involves the development of a holiday resort and it is unlikely that the structure will be removed.

Should the need arise in future to remove the structures wholly, the Applicant must consult with the Competent Authority to ensure compliance with legislation applicable at the time.

3 LEGISLATIVE REQUIREMENTS

The project Applicant is required to comply with all necessary legislation and policies applicable to development and management of the development. These include but are not limited to:

3.1 NATIONAL ENVIRONMENTAL MANAGEMENT ACT (NEMA, ACT 107 OF 1998)

The National Environmental Management Act (**NEMA**, Act 107 of 1998, as amended), makes provision for the identification and assessment of **activities** that are potentially detrimental to the environment and which require authorisation from the competent authority (in this case, the provincial Department of Environmental Affairs & Development Planning (DEA&DP)) based on the findings of an Environmental Impact Assessment (EIA).

NEMA embraces the notion of sustainable development as contained in the Constitution of South Africa (Act 106 of 1996) in that everyone has the right:

- to an environment that is not harmful to their health or wellbeing; and
- to have the environment protected for the benefit of present and future generations through reasonable legislative and other measures.

NEMA aims to provide for cooperative environmental governance by establishing principles for decision-making on all matters relating to the environment and by means of Environmental Implementation Plans (EIP) and Environmental Management Plans/Programmes (EMPr), of which this EMPr is one.

Principles contained in Section 2 of the NEMA, amongst other things, prescribe that environmental management must:

- In order of priority aim to: avoid, minimise or remedy disturbance of ecosystems and loss of biodiversity;
- Avoid degradation of the environment and avoid jeopardising ecosystem integrity;
- Pursue the best practicable environmental option by means of integrated environmental management;
- Protect the environment as the people's common heritage;
- Control and minimise environmental damage; and
- Pay specific attention to management and planning procedures pertaining to sensitive, vulnerable, highly dynamic or stressed ecosystems.

It is incumbent upon the landowner, to ensure that the abovementioned principles, entrenched in this EMPr are upheld and complied with.

3.2 ENVIRONMENT CONSERVATION ACT, 1989 (ECA)

The EIA regulations contained in the Environmental Conservation Act (ECA) have been replaced by NEMA. However, property owners must comply with the draft regulations pertaining to noise as published in the province of Western Cape Provincial Extraordinary Gazette as provision made in section 25 of the ECA), as well as Section 24 of the ECA regarding waste management and Section 20 of the ECA dealing with waste management under Part IV, Control of Environmental Pollution.

3.3 NATIONAL ENVIRONMENTAL MANAGEMENT: BIODIVERSITY ACT (NEM:BA) (ACT 10 OF 2004)

This Act controls the management and conservation of South African biodiversity within the framework of NEMA. Amongst others, it deals with the protection of species and ecosystems that warrant national protection, as well as the sustainable use of indigenous biological resources. Sections 52 & 53 of this Act specifically make provision for the protection of critically endangered, endangered, vulnerable and protected ecosystems that have undergone, or have a risk of undergoing, significant degradation of ecological structure, function or composition as a result of human intervention through threatening processes.

The National List of Threatened Ecosystems (Notice 1477 of 2009, Government Gazette No. 32689, 6 November 2009) was gazetted in 2014. The list of threatened terrestrial ecosystems supersedes the information regarding terrestrial ecosystem status in the National Spatial Biodiversity Assessment (NSBA) 2004 & 2011.

In addition to the management of ecosystems, this Act makes provision for the management and control of alien invasive vegetation. This includes the listing of invasive species that are a threat to natural ecosystems. These species must be strictly controlled and / or eradicated. Only indigenous vegetation should be permitted for landscaping.

National Waste Management Strategy

The National Waste Management Strategy presents the South African government's strategy for integrated waste management for South Africa.

It deals among others with: Integrated Waste Management Planning, Waste Information Systems, Waste Minimisation, Recycling, Waste Collection and Transportation, Waste Treatment, Waste Disposal and Implementing Instruments.

It is advisable that an integrated waste management system be adopted, which includes waste minimisation, waste recycling and the proper storage and disposal of waste, which does not impact of the health of the environment and human health.

All waste must be collected and disposed of at a waste facility. No waste material may be left on site once construction/maintenance is completed.

3.4 NATIONAL WATER ACT (NWA, ACT 36 OF 1998)

The National Water Act (NWA) gives effect to the constitutional right of access to water. The Act's overall purpose is to ensure that South Africa's water resources are protected, used and managed in ways which take into account a number of factors, including inter-generational equity, equitable access, redressing the results of past racial and gender discrimination, promoting sustainable and beneficial use, facilitating social and economic development, and providing for water quality and environmental protection.

The NWA makes persons who own, control, occupy or use land responsible for taking measures to prevent pollution of water resources, and empowers Government authorities to take measures to enforce this obligation.

3.5 NATIONAL FOREST ACT (ACT 84 OF 1998)

The NFA provides for the **protection of forests**, as well as **specific tree species**, quoting directly from the Act: "no person may cut, disturb, damage or destroy any protected tree or possess, collect, remove, transport, export, purchase, sell, donate or in any other manner acquire or dispose of any protected tree or any forest product derived from a protected tree, except under a licence or exemption granted by the Minister to an applicant and subject to such period and conditions as may be stipulated". The Department of Agriculture, Forestry & Fisheries (DAFF) is responsible for the implementation and enforcement of the NFA, which includes **prohibition of damage to indigenous**

trees in any natural forest without a licence (Section 7 of the NFA), as well as the prohibition of the cutting, disturbing, damaging destroying or removing **protected trees** without a licence (Section 15 of the NFA).

The purpose of the National Veld and Forest Fire Act is to **prevent and combat veld, forest and mountain fires** throughout the RSA and to provide institutions, methods and practices for achieving this purpose. Institutions include the formations of such bodies as **Fire Protection Associations** (FPA's) and **Working on Fire**. The Act provides the guidelines and constitution for the implementation of these institutions as well as their functions and requirements.

3.6 NATIONAL HERITAGE RESOURCES ACT (ACT 25 OF 1999)

The purpose of the National Heritage Resources Act is to:

- Introduce an integrated and interactive system for the management of the national heritage resources;
- Promote good government at all levels,
- Empower civil society to nurture and conserve their heritage resources so that they may be bequeathed to future generations;
- To lay down general principles for governing heritage resources management throughout South Africa;
- To introduce an integrated system for the identification, assessment and management of the heritage resources of South Africa;
- To establish the South African Heritage Resources Agency together with its Council to co-ordinate and promote the management of heritage resources at national level;
- To set norms and maintain essential national standards for the management of heritage resources in South Africa and to protect heritage resources of national significance;
- To control the export of nationally significant heritage objects and the import into South Africa of cultural property illegally exported from foreign countries;
- To enable the provinces to establish heritage authorities which must adopt powers to protect and manage certain categories of heritage resources;
- To provide for the protection and management of conservation-worthy places and areas by local authorities; and
- To provide for matters connected therewith.

3.7 OCCUPATIONAL HEALTH AND SAFETY ACT (ACT 85 OF 1993)

The Act provides for the health and safety of persons at work and for the health and safety of persons in connection with the use of plant and machinery; the protection of persons other than persons at work against hazards to health and safety arising out of or in connection with the activities of persons at work.

In terms of this Act, a Health and Safety Officer and Protocol must be implemented on any sites. The appointment of a Health and Safety Officer is the responsibility of the proponent and contractor and is included in this report to ensure due diligence on construction sites. It is the responsibility of the appointed HSO to conduct any required audits and as such only the appointment of an HSO will be auditable in terms of this document.

4 ENVIRONMENTAL IMPACTS & MITIGATIONS

The following specialist impact assessments / studies were undertaken for the proposal:

- Faunal Compliance Statement (Dr Jonathan Colville)
- Botanical Impact Assessment (Dr David McDonald)
- Biodiversity Impact Assessment (Dr David McDonald)

The following environmental impacts of the proposed activity were identified and considered during the environmental process, based on which the associated mitigation measures were recommended for implementation (to reduce negative impacts & enhance positive ones):

Specialist Assessments/Compliance Statement

Potential Impacts

- Loss of Vegetation - Removal of Hartenbos Dune Thicket (with consequent loss of habitat).
- Loss of Habitat and its Biodiversity - Removal of Hartenbos Dune Thicket (with consequent loss of habitat and ecological functionality).

4.1 MITIGATIONS

Table 2: List of Mitigation Measures & Associated Management Requirements

Mitigation	Condition of Approval	Included in EMPr	Construction Phase	Operational /Maintenance Phase	Decommissioning Phase
Mitigations / Recommendations					
Applicant must appoint an ECO to oversee construction.	✓	✓	✓	✓	
The stormwater outlet structures, must be designed adequately to dissipate the energy.		✓	✓		
Clearly demarcate No-Go areas (protected indigenous tree species).		✓	✓		
Stockpiles of materials must be placed on as flat as possible surface and protected (through use of sandbags and/or tarpaulins).		✓	✓		
Prevent uncontrolled access of vehicles into the development site.		✓	✓	✓	
Demarcate the area(s) chosen for the stockpiling of imported materials and put-up notices declaring what must be stockpiled.		✓	✓	✓	
Development of a construction schedule.		✓	✓		
Oil and fuel leaks of excavators and all other machinery must be checked daily.		✓	✓	✓	
Bunds should be placed around refuelling, fuel storage and servicing areas. These areas must not be located within any natural drainage areas or preferential flow paths.		✓	✓	✓	

Mitigation	Condition of Approval	Included in EMPr	Construction Phase	Operational /Maintenance Phase	Decommissioning Phase
Chemical toilets (1 toilet / 10 persons).		✓	✓		
Waste from chemical toilets must be disposed of regularly by a registered waste contractor.		✓	✓		
No mixing of cement / concrete on bare ground.		✓	✓		
Instruct workers & contractors properly of the environment (environmental inductions).		✓	✓	✓	
All waste generated on-site must be adequately managed.		✓	✓		
Separation and recycling of different waste materials should be supported.		✓	✓		
Scouring or undercutting caused by stormwater outlets must be rehabilitated following the inputs of an aquatic ecologist.		✓		✓	
Relocation of geophytes from the development footprint (permit must be acquired from CapeNature).		✓	✓		
All construction activities must take place within the development footprint.		✓	✓		
Areas outside the development footprint must be avoided.		✓	✓		
Any areas within the development footprint that will not be used later should be rehabilitated with natural vegetation native to the area.		✓	✓		
Undertake vegetation clearing during the dry season.		✓	✓		
Keep vegetation cut low, but not eradicated, along firebreaks.		✓	✓		
Only clear vegetation where absolutely necessary.		✓	✓		
Best Practise					
Construction work must take place during normal work hours.		✓	✓	✓	
Traffic management must be in place during construction		✓	✓		

5 RESPONSIBILITIES

This section deals with the responsibilities of various parties during the Construction Phase of any development.

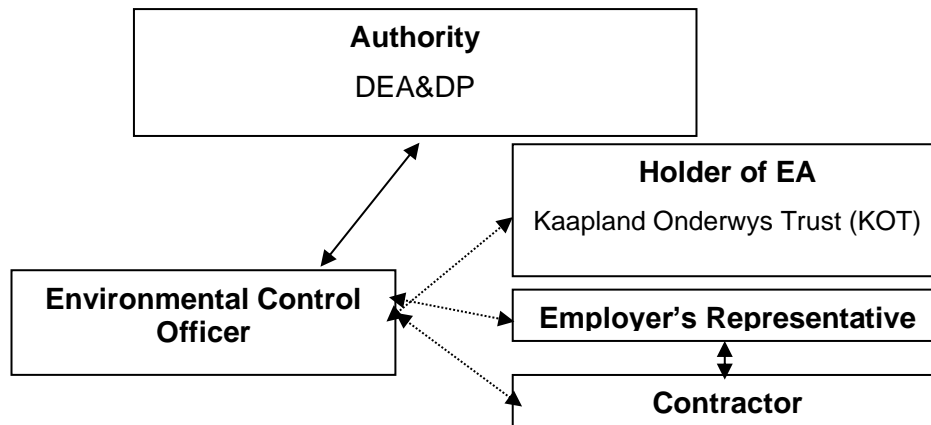


Figure 3: Responsibilities.

5.1 HOLDER OF THE EA

The holder of the EA / property owner is the overseeing entity responsible for ensuring that all activities undertaken on the property comply with the Environmental Authorisation (EA) and associated Environmental Management Programme (EMPr) (and any other approval / licence / permit), as well as the management and maintenance of the open space areas.

The responsibilities of the holder of the EA / property owner include, but are not limited to the following:

- Ensure that **all tender documentation** include reference to, and the need for compliance with, the EA and EMPr as well as any other legally binding documentation, which include and are not limited to Approval/s.
- Be conversant with, and ensure that all Contractors, Sub-contractors, Engineers (and future senior site managers / personnel) are made aware of, and understand the conditions and recommendations, contained in the abovementioned documentation;
- Ensure that all Contractors, Sub-contractors and Engineers (during construction activities) are made aware of their 'Duty of Care to the Environment' and that any damage or degradation of the natural environment within the bounds of the property will not be tolerated and must be dealt with / remedied at the cost of the perpetrator;
- Take remedial and/or disciplinary action in circumstances where persons are found to be in contravention of the abovementioned legally binding documentation.

5.2 ENGINEERS AND CONTRACTORS

The Engineers and Contractors are often the parties responsible for physically carrying out the activities for which majority of the recommendations in this EMPr are intended. Service providers and Contractors include: services, building contractors, 'handy-men' and engineers overseeing the installation and maintenance of services etc. The responsibilities indicated here are also relevant to Sub-Contractors.

The responsibilities of these parties include but are not limited to the following:

- Be conversant and compliant with the EA, the EMPr, and any relevant License, Permit or any legally binding documentation relevant to their operations;

- Have a responsibility to adhering to any conditions and recommendations laid out in above mentioned documentation;
- Prevent actions that may cause harm to the environment;
- Be responsible for any remedial activities in response to an environmental incident within their scope of influence;
- Liaise with the holder of the EA in complying with the EMPr, and in the event that any industry regulated standards are in contradiction with the EMPr or any other authorisations.
- Review and amend to any construction activities to align with the EMPr and Best Practice Principles;
- Ensure compliance of all site personnel and / or visitors to the EMPr and any other authorisations.

5.3 ENVIRONMENTAL CONTROL OFFICER (ECO)

It is recommended that a suitably qualified Environmental Control Officer (ECO) be appointed to oversee all activities for the duration of the construction phase as well as any maintenance work that must be undertaken that will involve earthworks or machine works. The ECO must have at least 3 years' experience and proven competency as an ECO.

The responsibilities of the ECO include but are not limited to the following:

- Provide environmental induction training to Contractors on site prior to construction activities commencing
- Provide maintenance, update and review of the EMPr if necessary;
- Liaison between the Project Holder of the EA, Contractors, Authorities and other lead stakeholders on all environmental concerns, including the implementation of the EMPr;
- Compilation of Environmental Control Reports (ECR) to ensure compliance with the EA, EMPr and duty of care requirements, where necessary;
- Compilation of the Environmental Audit Report or Environmental Completion Statement, after completion of construction (or as otherwise defined in the Environmental Authorisation), where necessary;
- Ensuring / guiding and monitoring compliance with the EA and EMPr and any legally binding documentation;
- Facilitating consultation with relevant environmental authorities (e.g. DEA&DP, DFFE, CapeNature or Municipality);
- Facilitating the application for any required amendment of the EA/EMPr;
- Provide guidance and interpretation of the EA and EMPr where necessary;
- Issuing site instructions to the contractor for corrective actions required;
- The ECO is required to conduct regular site visits for the duration of the construction period, in order to ensure the Contractor receives the necessary induction and that all procedures are in place. Additional visits may be undertaken in the event of any unforeseen environmental accidents;
- The duration and frequency of these visits may be increased or decreased at the discretion of the ECO;
- Attendance of site meetings if required;
- Maintain a record of environmental incidents (e.g. spills, impacts, legal transgressions etc.) as well as corrective and preventative measures taken. This information must also be included in the ECR;
- Maintain a public complaints register in which all complaints and action taken must be recorded. This information must also be included in the ECR.

5.4 ECO SITE VISIT FREQUENCY

The following site frequency for ECO site visits has been determined:

- Weekly during pre-construction and construction phases.

Ad hoc site visits may be undertaken in the event of any incidents or specific requests from the project holder of the EA or project team.

5.5 ENVIRONMENTAL INDUCTION & TRAINING

The holder of the EA in consultation with the Contractor shall ensure that adequate environmental awareness training of senior site personnel takes place and that all construction workers receive an induction presentation on the importance and implications of the EA and EMPr. The presentation shall be conducted, as far as is possible, in the employees' language of choice. The Contractor must provide a translator from their staff for the purpose of translating, if this is deemed necessary.

As a minimum, training must include:

- Explanation of the importance of complying with the EA and EMPr and the employees accountability;
- Discussion of the potential environmental impacts of construction activities;
- The benefits of improved personal performance;
- Employees' roles and responsibilities, including emergency preparedness ;
- Explanation of the mitigation measures that must be implemented when carrying out their activities;
- Explanation of the specifics of this EMPr and its specification (no-go areas, etc.);
- Explanation of the management structure of individuals responsible for matters pertaining to the EMPr.

Where staff turnover is high and with additional appointment of sub-contractors, it may be necessary to undertake additional induction training sessions. The Contractor must keep records of all environmental training sessions, including names, dates and the information presented.

6 PRE-CONSTRUCTION DESIGN CONSIDERATIONS

It is recommended that sustainable design considerations are implemented during the planning phase to ensure that the impacts associated with the development are avoided, minimised or managed before construction commences.

6.1 <u>STORMWATER MANAGEMENT PREPARATION</u>					
Management Statement			Impacts & Risks Avoided		
To prepare the site to minimise the negative impacts of stormwater.			Damage to the environment caused by stormwater runoff.		
Management Actions					
a. Final design of the stormwater system must take place prior to construction to ensure timeous implementation.					
Method of monitoring implementation	Frequency of Monitoring	Responsible Party for implementing management action	Time period	Mechanism for monitoring Compliance	Programme for reporting on Compliance
Site Plans	Once off	Architect / Engineer	Prior to construction	Audit	Once off

6.2 <u>WATER RESOURCE PROTECTION</u>					
Management Statement			Impacts & Risks Avoided		
To minimise the use of scarce water resources by improving consumption methods.			Unsustainable or wasteful use of water for construction and operation purposes.		
Management Actions					
a. Rainwater harvesting must be incorporated into the designs. All rainwater tanks must be shown on building plans.					
Method of monitoring implementation	Frequency of Monitoring	Responsible Party for implementing management action	Time period	Mechanism for monitoring Compliance	Programme for reporting on Compliance

Site Plans	Once off	Architect / Engineer	Prior to construction	Audit	Once off
b. Water efficiency must be incorporated into the design of the units.					
Method of monitoring implementation	Frequency of Monitoring	Responsible Party for implementing management action	Time period	Mechanism for monitoring Compliance	Programme for reporting on Compliance
Site Plans	Once off	Architect	Prior to construction	Audit	Once off

Dual Flush Toilets

Conservative estimates have shown that a saving of more than 22 000 liters per household can be achieved annually with the installation of dual flush toilets (Aquanotion, 2008). All households and ablution facilities should be fitted with dual flush systems.

Low flow shower heads

The installation of low flow shower heads can not only reduce water consumption by up to 50%, but also the energy required for water heating by up to 50% (Eartheasy, 2008).

It has been estimated that a saving of up to 57 000 liters of water per annum per household can be achieved through the installation of low flow shower heads. Low flow shower heads make use of either aerators or pulse systems to reduce the flow without compromising the quality of the shower. The choice of shower head is up to the individual owner, but must have a flow of less than seven liters per minute.

Low flow Taps

Low flow tap use aerators to reduce the flow of the water. These are either built into the faucet or added as an aftermarket product. The faucets in bathrooms should have a peak flow of less than 10 liters per minute.

It is not necessary to install aerators in kitchen sinks as they are seldom run without a plug. All bathroom basins must be fitted with low flow faucets.

Washing machines

It is recommended that all washing machines that are to be installed in shared facilities should be front loading washing machines as opposed to top loading washing machines. Apart from much lower energy and water requirements, front loader washing machines have a number of advantages that make them a better environmental choice:

- **Less wear and tear on washed materials** – Washed materials therefore last longer and result in a net resource saving;
- **Faster drying times** - Because of the horizontal axis and faster spin speeds, more water is removed and the materials dry faster which results in energy saving if a clothes dryer is used.;
- **Quieter operation** – Therefore less noise pollution; and
- **Less detergent** - Far less is required compared to top loaders. Fewer chemicals therefore reach treatment plants and ultimately waterways.

Geyser and pipe insulation

Apart from the savings in terms of energy as detailed below, insulating geysers and pipes save water, as shorter periods of running the tap to get hot water are required.

All structures should have insulation on geysers and all hot water pipes.

Waterwise Landscaping

Waterwise landscaping principles must be incorporated into the detailed landscaping plans. The following principles apply to waterwise gardening:

- Grow water-wise plants – generally the best suited plants are those indigenous to the area, as they seldom need additional watering;
- Group plants according to their water needs – this avoids wasting water on plants that don't need it;
- Consider the quality and type of the lawn. Lawns use unacceptable amounts of water, so consider reducing lawn areas to a minimum. Use tougher, low-water lawn types such as Buffalo (coastal areas) or Kweek (inland) rather than Kikuyu.
- Maintain the garden – remove unwanted plants, plant more perennials than summer annuals, as they have deeper root systems and so need less watering.
- Improve the soil and mulch. Soil water-holding capacity is improved by higher organic matter content. Mulching (covering the soil with a thick layer of bark, compost, straw etc.) keeps the soil much more moist.
- Plant in the right season – For winter rainfall areas this is in autumn and early winter so the plants have a chance to develop their root systems before the dry season. In summer rainfall areas it is spring and early summer for the same reason.
- Water correctly – avoid watering during the heat of the day or in windy conditions.
- The best irrigation system is drip irrigation – it uses 25% of water used by normal irrigation systems with the same effect, and can even be placed under lawns.

Grey Water

Grey water is the water that comes from the bath, shower, basins, laundry and the kitchen sink. It is not to be confused with Black water, which is sewage that comes from the toilet. Black water is toxic and requires very specific methods of treatment in order to be safe for re-use. Grey water, however, can easily be recycled and re-used for a variety of uses. These include:

- Irrigation of gardens;
- Water for flushing toilets;
- Any outdoor use;
- Dampening dusty areas or roads.

Grey water systems require precise methods to clean the water. There are various companies and organizations that can assist with implementing a grey water system.

6.3 ENERGY RESOURCE PROTECTION

Management Statement		Impacts & Risks Avoided			
To minimise the use of energy resources by improving consumption methods.		Excessive and unnecessary energy consumption.			
Management Actions					
a. Incorporate energy efficiency into the design of the facility.					
Method of monitoring implementation	Frequency of Monitoring	Responsible Party for implementing management action	Time period	Mechanism for monitoring Compliance	Programme for reporting on Compliance

Energy saving checklist	Once off	Owner	Ad hoc	Audit	Once off
-------------------------	----------	-------	--------	-------	----------

Solar heating water systems


Solar heated water systems are an innovative way of producing hot water without putting additional pressure on gas or municipal power supply. There are many different types available on the market, and home owners should consider all their requirements (number of people using facility, location of house, angles of roof) before making a choice.

Energy Efficient Lighting

In terms of Best Practice, it is required that energy saving lighting fixtures be used throughout the entire development. It is therefore specified that Light Emitting Diode (LED) or Compact Fluorescent (CF) lighting be used as opposed to incandescent lighting. This is required for all internal and external lighting, including street lighting. Proximity switches should be used in areas where lighting for pedestrians is required.

NO external High Pressure Sodium (HPS) or Metal Halide (MH) spot or floodlights should be installed.

CF lighting uses quantities of mercury in the bulbs and tubes which pose serious environmental hazards. The mercury from one CF bulb can pollute many thousand litres of water if not treated correctly (Eden District Municipality, 2011). CF lighting (energy saving bulbs and tubes) must be correctly disposed of at registered Hazardous waste sites. Companies like Pick n Pay and Woolworths offer facilities to collect CF bulbs for recycling and disposal. The following should be considered when handling CF bulbs (eHow Home, 2011):

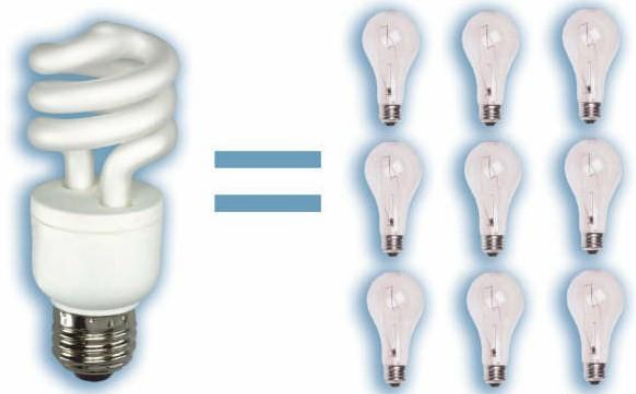

Disposing of Burnt Out Bulbs

- Seal the bulb inside two plastic bags, or one thick freezer bag, before disposal.
- Find the nearest recycling station that handles hazardous materials. Check with your city's municipal office to see if there is a recycling program in your town.
- Take the bulbs to the recycling station. Ask the people there about the process of giving them your bulbs and follow all their instructions.
- Tell everyone you know who is using energy efficient bulbs how to properly dispose of them as the use of these bulbs is growing.

If a Bulb Breaks

- Open a window and leave the room. Let no one inside for at least 15 minutes.
- Collect the fragments and powder with stiff paper or cardboard. Wear disposable rubber gloves. Do not use a vacuum cleaner.
- Clean the entire area with a wet wipe or wet paper towel. Use adhesive tape to collect excess powder.
- Seal all pieces and cleanup materials in a plastic bag. Follow the above procedures on disposal or recycling. Wash your hands completely afterward.
- Dispose of the vacuum bag in the same manner the next time you vacuum the area. If it's a canister vacuum, wipe it completely clean.

Energy Efficient Appliances

Energy efficient appliances are becoming widely available. Follow the Energy Guide labels on appliances to help selection of correct models. Any appliance that has to heat up water or air will use more energy, as will an appliance that boasts additional extras such as ice making, dispensing and auto defrosting on fridges or heat drying on dishwashers.

Solar Cooling Systems

Where required by homeowners, the home owner should consider the use of solar cooling systems such as absorption or adsorption chillers as opposed to conventional air conditioning units.

Evaporative Cooling Systems

Consideration should be given to evaporative cooling systems as these cut down considerably on energy usage for appliances such as air conditioners. Furthermore, the system ensures that fresh air circulates within housing units, which improves on environmental health risks.

Fresh air is drawn from outside the house (the hotter the better) and passes through moistened pads which cools it down and filters it before flowing through outlets in the house.

There are certain parameters required for evaporative cooling systems, which should be thoroughly investigated prior to installation.

Geyser and pipe insulation

Apart from the savings in terms of energy as detailed below, insulating geysers and pipes save water, as shorter periods of running the tap to get hot water are required.

All structures should have insulation on geysers and all hot water pipes.

6.4 DEMARCATION OF WORK AND NO-GO AREAS

Management Statement		Impacts & Risks Avoided			
To clearly define the work area and avoid impacting on non-work areas.		Negative construction impacts on natural and rehabilitated areas.			
Management Actions					
a. Clearly identify and demarcate the development area, area of works and spoiling areas.					
Method of monitoring implementation	Frequency of Monitoring	Responsible Party for implementing management action	Time period	Mechanism for monitoring Compliance	Programme for reporting on Compliance
Method Statement	Once off	Developer / contractor	Pre implementation	Audit	Once off
b. Fuel and chemicals may only be stored in a designated work area.					
Method of monitoring implementation	Frequency of Monitoring	Responsible Party for implementing management action	Time period	Mechanism for monitoring Compliance	Programme for reporting on Compliance
Method Statement	Once off	Developer / contractor	Pre implementation	Audit	Once off
c. Provide on-site sanitation and rest areas for personnel.					

Method of monitoring implementation	Frequency of Monitoring	Responsible Party for implementing management action	Time period	Mechanism for monitoring Compliance	Programme for reporting on Compliance
Method Statement	Once off	Developer / contractor	Pre implementation	Audit	Once off

7 CONSTRUCTION CONSIDERATIONS

These Construction Phase requirements are aimed at using Best Practise Principles and / or specialist recommendations to manage the impacts on the environment during the construction of the development.

Table 3: Site Clearance Methodology.

No	Action	Scheduling
1	Survey approved layout on site.	Prior to construction
2	Establish site camp and material stockpile sites (incl. waste disposal area, portable toilets etc. The construction camp and necessary ablution facilities meant for construction workers must not be in any of the delineated watercourses or wetland areas (including 20m buffer).	Prior to construction.
3	Demarcate work areas using correct demarcation methods.	Prior to construction.
4	Demarcate protected areas as no-go areas .	Prior to construction.
5	Erosion control measures must be put in place prior to any construction activities that would result in soil being exposed.	Prior to construction.
6	Weather forecasts from the South African Weather Bureau of up to three days in advance must be monitored on a daily basis to avoid exposing soil, works or materials during a storm event. This must be considered in conjunction with tide tables for beach construction work.	Construction
7	Commence with mechanical vegetation clearing within the demarcated work areas only.	Construction
8	Vegetation clearing should occur in parallel with the construction progress to minimise erosion and/or run-off. Large tracts of bare soil will either cause dust pollution or quickly erode and then cause sedimentation in the lower portions of the catchment.	Construction
9	Any biomass from the clearing activities must be stockpiled within the development footprint at an area / areas approved by the ECO. It is recommended that the biomass must be chipped in situ and stockpiled within designated areas within the footprint. Alternatively, it must be removed and taken to an approved disposal site for biomass. NO DUMPING IS ALLOWED.	Construction
10	Any cleared areas that will not be immediately constructed or planted, must be covered with the wood chips or other mulch to prevent wind erosion.	Construction

7.1 <u>STORMWATER MANAGEMENT</u>					
Management Statement/Outcome			Impacts & Risks Avoided		
To minimise the generation of contaminated stormwater.			Minimise sedimentation, erosion and / or undercutting.		
Management Actions					
d. Divert stormwater by placing sand bangs in the proposed area of construction which prevent the area from being saturated.					
Method of monitoring implementation	Frequency of Monitoring	Responsible Party for implementing management action	Time period	Mechanism for monitoring Compliance	Programme for reporting on Compliance
Method Statement	Once off	Developer / contractor	Pre implementation	Audit	Once off
<p>Any areas that are identified by the ECO as being prone to erosion must be suitably protected. During construction, the Contractor shall protect all areas susceptible to erosion by installing necessary temporary and permanent drainage works as soon as possible and by taking any other measures necessary to prevent stormwater from concentrating in streams and scouring slopes, banks, etc.</p> <p>Any erosion channels developed during construction on steep slopes must be backfilled, compacted and restored to an acceptable condition.</p> <p>Stabilisation of cleared areas to prevent and control erosion and/or sedimentation shall be actively managed. Consideration and provision shall be made for the following methods (or combination thereof): brush cut packing, mulch or chip cover, straw stabilising, watering, planting/sodding, soil binders and anti-erosion compounds, mechanical cover or packing structures (including the use of geofabric, log/pole fencing, etc.). Traffic and movement over stabilised areas shall be restricted and controlled, and damage to stabilised areas shall be repaired and maintained.</p> <p>In areas where construction activities have been completed and where no further disturbance would take place, rehabilitation and re-vegetation should commence as soon as possible. A suitable rehabilitation method statement must be submitted to the ECO for approval.</p>					
7.2 <u>DUST CONTROL</u>					
Management Statement/Outcome			Impacts & Risks Avoided		
To ensure there is no health risk or loss of amenity due to emission of dust to the environment.			Ensure land coverage with biomass chips / vegetation / damping to minimise dust.		
Management Actions					

a. Implement a dust prevention strategy, developed at the project planning stage.					
Method of monitoring implementation	Frequency of Monitoring	Responsible Party for implementing management action	Time period	Mechanism for monitoring Compliance	Programme for reporting on Compliance
Method Statement	Once off	Developer / contractor	Pre implementation	Audit	Once off

The strategy should include the following amongst others:

- Speed control to minimise dust on site.
- During dry, dusty periods haul roads should be kept dampened to prevent excess dust. No potable water or seawater may be used for damping haul roads.
- Exposed stockpile materials must be adequately protected against wind (covered), and should be sited taking into consideration the prevailing wind conditions.
- Trucks bringing in materials must be covered to prevent dust and small particles escaping and potentially causing damage to people and property.

7.3 NOISE

Management Statement/Outcome	Impacts & Risks Avoided
To ensure nuisance from noise and vibration does not occur.	Nuisance impacts to neighbours and visitors.

Management Actions

a. Fit and maintain appropriate mufflers on earth-moving and other vehicles on the site.					
Method of monitoring implementation	Frequency of Monitoring	Responsible Party for implementing management action	Time period	Mechanism for monitoring Compliance	Programme for reporting on Compliance
As required	Initially when vehicle or machinery is introduced to the site and thereafter monthly. As required if complaints registered.	Contractor	During construction and operation	Audit	As required
b. Enclose noisy equipment such as generators and pumps.					

Method of monitoring implementation	Frequency of Monitoring	Responsible Party for implementing management action	Time period	Mechanism for monitoring Compliance	Programme for reporting on Compliance
As required	Initially when vehicle or machinery is introduced to the site and thereafter monthly. As required if complaints registered.	Contractor	During construction	Audit	As required

c. Provide noise attenuation screens, where appropriate.

Method of monitoring implementation	Frequency of Monitoring	Responsible Party for implementing management action	Time period	Mechanism for monitoring Compliance	Programme for reporting on Compliance
As required	Initially when vehicle or machinery is introduced to the site and thereafter monthly. As required if complaints registered.	Contractor	During construction	Audit	As required

d. Where an activity is likely to cause a noise nuisance to nearby residents, restrict operating hours to between 7 am and 6 pm weekdays and 7 am to 1 pm Saturday, except where, for practical reasons, the activity is unavoidable.

Method of monitoring implementation	Frequency of Monitoring	Responsible Party for implementing management action	Time period	Mechanism for monitoring Compliance	Programme for reporting on Compliance
As required	As required if complaints registered.	Contractor	During construction	Audit	As required

7.4 TRAFFIC CONTROL

Management Statement/Outcome	Impacts & Risks Avoided
To manage and minimise the nuisance effect created by construction traffic.	The development entrance access will be via H.C.Botha Street and construction traffic is likely to temporarily affect users H.C. Botha Street and Morrison Road.

Management Actions					
a. Implement a traffic management strategy during construction.					
Method of monitoring implementation	Frequency of Monitoring	Responsible Party for implementing management action	Time period	Mechanism for monitoring Compliance	Programme for reporting on Compliance
Method Statement	Daily	Contractor	During construction	Audit	As required
<ul style="list-style-type: none"> Construction related activities should be timed where possible to avoid peak periods. No construction workers, apart from security personnel, should be allowed to stay on site overnight. Contractors appointed by the developer must ensure that workers are transported to and from the site daily. Construction related activities should comply with all relevant building regulations. In this regard activities on site should be restricted to between 07h00 and 18h00 during weekdays and 08h00 and 13h00 on Saturdays. No work should be permitted after 13h00 on Saturdays and on Sundays. Temporary access to be rehabilitated once construction is complete. 					
7.5 <u>WASTE MANAGEMENT</u>					
Management Statement/Outcome			Impacts & Risks Avoided		
To minimise the waste load discharged to the environment.			Improve waste disposal methods during construction. Reduce waste volumes to landfill sites.		
Management Actions					
a. Reduce wastes by selecting, in order of preference, avoidance, reduction, reuse and recycling.					
Method of monitoring implementation	Frequency of Monitoring	Responsible Party for implementing management action	Time period	Mechanism for monitoring Compliance	Programme for reporting on Compliance
Record of volumes of material removed	As required	Contractor	As required	Audit	Records
b. Maintain a high quality of housekeeping and ensure that materials are not left where they can be washed or blown away to become litter.					
Method of monitoring implementation	Frequency of Monitoring	Responsible Party for implementing management action	Time period	Mechanism for monitoring Compliance	Programme for reporting on Compliance

Photographic	Weekly	Contractor	As required	Audit	Records
c. Provide bins for construction workers and staff at locations where they consume food.					
Method of monitoring implementation	Frequency of Monitoring	Responsible Party for implementing management action	Time period	Mechanism for monitoring Compliance	Programme for reporting on Compliance
Photographic	Weekly	Contractor	As required	Audit	Records
d. Conduct ongoing awareness with staff of the need to avoid littering.					
Method of monitoring implementation	Frequency of Monitoring	Responsible Party for implementing management action	Time period	Mechanism for monitoring Compliance	Programme for reporting on Compliance
Induction	Once off	Contractor	As required	Audit	Attendance register
7.6 STOCKPILE MANAGEMENT					
Management Statement/Outcome			Impacts & Risks Avoided		
To manage soil stockpiles so that dust and sediment in run-off are minimised.			Pollution due to dust and sediment run off.		
Management Actions					
a. Minimise the number of stockpiles, and the area and the time stockpiles are exposed.					
Method of monitoring implementation	Frequency of Monitoring	Responsible Party for implementing management action	Time period	Mechanism for monitoring Compliance	Programme for reporting on Compliance
Photographic	As required	Contractor	As required	Audit	Records

b. Keep topsoil and underburden stockpiles separate.					
Method of monitoring implementation	Frequency of Monitoring	Responsible Party for implementing management action	Time period	Mechanism for monitoring Compliance	Programme for reporting on Compliance
Visual inspection of stockpiles	Daily when stripping topsoil	Contractor	Continuously during construction	Audit	Records
c. Ensure that stockpiles and batters are designed with slopes no greater than 2:1 (horizontal/vertical).					
Method of monitoring implementation	Frequency of Monitoring	Responsible Party for implementing management action	Time period	Mechanism for monitoring Compliance	Programme for reporting on Compliance
Visual inspection of stockpiles	As required	Contractor	Continuously during construction	Audit	Monthly
d. Stabilise stockpiles and batters that will remain bare for more than 28 days by covering with mulch or anchored fabrics or seeding with sterile grass.					
Method of monitoring implementation	Frequency of Monitoring	Responsible Party for implementing management action	Time period	Mechanism for monitoring Compliance	Programme for reporting on Compliance
Visual inspection of stockpiles	As required	Contractor	Continuously during construction	Audit	Monthly
e. Establish sediment controls around unstabilised stockpiles and batters.					
Method of monitoring implementation	Frequency of Monitoring	Responsible Party for implementing management action	Time period	Mechanism for monitoring Compliance	Programme for reporting on Compliance
Visual inspection of stockpiles	As required	Contractor	Continuously during construction	Audit	Monthly

f. Suppress dust on stockpiles and batters, as circumstances demand.					
Method of monitoring implementation	Frequency of Monitoring	Responsible Party for implementing management action	Time period	Mechanism for monitoring Compliance	Programme for reporting on Compliance
Visual inspection of stockpiles	As required	Contractor	Continuously during construction	Audit	Monthly
7.7 <u>STORING FUELS & CHEMICALS</u>					
Management Statement/Outcome			Impacts & Risks Avoided		
To ensure that fuel and chemical storage is safe, and that any materials that escape do not cause environmental damage.			Avoid hydrocarbon pollution to soil and watercourses / coastal environments.		
Management Actions					
a. Minimise fuels and chemicals stored onsite.					
Method of monitoring implementation	Frequency of Monitoring	Responsible Party for implementing management action	Time period	Mechanism for monitoring Compliance	Programme for reporting on Compliance
Method statement	As required	Contractor	As required	Audit	Method statement records
b. Install bunds and take other precautions to reduce the risk of spills.					
Method of monitoring implementation	Frequency of Monitoring	Responsible Party for implementing management action	Time period	Mechanism for monitoring Compliance	Programme for reporting on Compliance
Method statement	As required	Contractor	As required	Audit	Method statement records

c. Implement a contingency plan to handle spills, so that environmental damage is avoided.					
Method of monitoring implementation	Frequency of Monitoring	Responsible Party for implementing management action	Time period	Mechanism for monitoring Compliance	Programme for reporting on Compliance
Method statement	As required	Contractor	As required	Audit	Method statement records

7.8 MINIMISING EROSION

Management Statement/Outcome	Impacts & Risks Avoided
To minimise the quantity of soil lost during construction due to land-clearing.	Avoid overland flow by capture and store water from roof. Avoid siltation by installing silt traps.

Management Actions

a. Schedule measures to avoid and reduce erosion by phasing the work program to minimise land disturbance in the planning and design stage.

Method of monitoring implementation	Frequency of Monitoring	Responsible Party for implementing management action	Time period	Mechanism for monitoring Compliance	Programme for reporting on Compliance
Method statement	As required	Contractor	As required	Audit	Method statement records

b. Keep the areas of land cleared to a minimum, and the period areas remain cleared to a minimum

Method of monitoring implementation	Frequency of Monitoring	Responsible Party for implementing management action	Time period	Mechanism for monitoring Compliance	Programme for reporting on Compliance
Method statement	As required	Contractor	As required	Audit	Method statement records

c. Base control measures to manage erosion on the vulnerability of cleared land to soil loss, paying particular attention to protecting slopes.					
Method of monitoring implementation	Frequency of Monitoring	Responsible Party for implementing management action	Time period	Mechanism for monitoring Compliance	Programme for reporting on Compliance
Method statement	As required	Contractor	As required	Audit	Method statement records
d. Mulch, roughen and seed cleared slopes and stockpiles where no works are planned for more than 28 days, with sterile grasses.					
Method of monitoring implementation	Frequency of Monitoring	Responsible Party for implementing management action	Time period	Mechanism for monitoring Compliance	Programme for reporting on Compliance
Method statement	As required	Contractor	As required	Audit	Method statement records
e. Keep vehicles to well-defined haul roads.					
Method of monitoring implementation	Frequency of Monitoring	Responsible Party for implementing management action	Time period	Mechanism for monitoring Compliance	Programme for reporting on Compliance
Site plan	As required	Contractor	As required	Audit	Final site plan
f. Rehabilitate cleared areas promptly.					
Method of monitoring implementation	Frequency of Monitoring	Responsible Party for implementing management action	Time period	Mechanism for monitoring Compliance	Programme for reporting on Compliance
Visual / photographic	As required	Contractor	Continuously during construction	Audit	Final Rehabilitation statement
7.9 REHABILITATION & BOTANICAL MANAGEMENT					
Management Statement/Outcome			Impacts & Risks Avoided		

To ensure that degradation to existing botanical/aquatic components are minimised and that any rehabilitation is undertaken with conservation orientated approach.			To minimise the disturbance to existing flora. To minimise the introduction and/or spread of weed species.		
Management Actions					
a. Demarcate sensitive areas to avoid damage during construction.					
Method of monitoring implementation	Frequency of Monitoring	Responsible Party for implementing management action	Time period	Mechanism for monitoring Compliance	Programme for reporting on Compliance
Method statement	As required	Contractor / Owner	Continuously	Audit	Visual / photographic
b. Rehabilitation and landscaping may only make use of indigenous vegetation.					
Method of monitoring implementation	Frequency of Monitoring	Responsible Party for implementing management action	Time period	Mechanism for monitoring Compliance	Programme for reporting on Compliance
Visual / photographic	As required	Contractor / Owner	Continuously	Audit	Visual / photographic
7.10 <u>FAUNA MANAGEMENT</u>					
Management Statement/Outcome			Impacts & Risks Avoided		
To ensure that impacts to native faunal species is minimised and / or avoided.			To minimise the impact to fauna.		
Management Actions					
a. Prevent unnecessary mortalities of indigenous fauna					
Method of monitoring implementation	Frequency of Monitoring	Responsible Party for implementing	Time period	Mechanism for monitoring Compliance	Programme for reporting on Compliance

		management action			
Ad hoc	As required	Contractor	Continuously	Audit	Visual / photographic

7.11 SOCIAL REQUIREMENTS

Management Statement/Outcome	Impacts & Risks Avoided
To ensure equitable, fair and safe social interaction on construction sites.	Loss of employment opportunities to the region.

Management Actions

- a. It is strongly recommended that the Contractor make use of local labour as far as possible for the construction phase of the project.

Method of monitoring implementation	Frequency of Monitoring	Responsible Party for implementing management action	Time period	Mechanism for monitoring Compliance	Programme for reporting on Compliance
Employment records	Ad hoc	Contractor	Ad hoc	Audit	Once off

- b. Theft and other crime associated with construction sites is not only a concern for surrounding residents, but also the Developer and the Contractor.

Method of monitoring implementation	Frequency of Monitoring	Responsible Party for implementing management action	Time period	Mechanism for monitoring Compliance	Programme for reporting on Compliance
Site records	Ad hoc	Contractor	Ad hoc	Audit	Once off

Targets

- The contractor should endeavour to source local suppliers.
- The contractor must ensure that suitable procurement policies are in place that supports local economic growth.
- Locally manufactured products must be used as far as possible.

Site Security

Theft and other crime associated with construction sites is not only a concern for surrounding residents, but also the developer and the contractor.

Considering this, contractors need to be proactive in order to curtail theft and crime on and resulting from the construction site. It is recommended that the contractor develop a jobsite security plan prior to commencement of construction. This jobsite security plan should take into account protection of the construction site from both internal and external crime elements as well as the protection of surrounding communities from internal crime elements. All incidents of theft or other crime should be reported to the South African Police Service, no matter how seemingly insignificant.

7.12 METHOD STATEMENTS

Management Statement/Outcome	Impacts & Risks Avoided
To ensure efficient communication mechanisms in the implementation of environmental performance requirements.	Prevention of potential impacts are avoided during construction by means of correct communication.

Management Actions

- a. Method statements are written submissions by the Contractor to the ECO in response to the requirements of this EMP or to a request by the ECO. The Contractor shall be required to prepare method statements for several specific construction activities and/or environmental management aspects.

Method of monitoring implementation	Frequency of Monitoring	Responsible Party for implementing management action	Time period	Mechanism for monitoring Compliance	Programme for reporting on Compliance
Method statement	Ad hoc	Contractor	As required	Audit	Once off

Based on the specifications in this EMP, the following method statements are required as a minimum (more method statements may be requested as required at any time under the direction of the ECO):

- Demarcation of No-Go areas
- Site clearing
- Hazardous substances and their storage.
- Materials requirements and sourcing.
- Solid waste control system.
- Fire control and emergency procedures
- Petroleum, chemical, harmful and hazardous materials storage, if any.
- Stormwater Management.
- Erosion Control.

7.13 HEALTH AND SAFETY

The Contractor must ensure compliance with the Occupational Health and Safety (No. 85 of 1993). Of key importance is the following (Section 8 of the aforesaid act):

8. General duties of employers to their employees:

- Every employer shall provide and maintain, as far as is reasonably practicable, a working environment that is safe and without risk to the health of his employees.
- Without derogating from the generality of an employer's duties under subsection (1), the matters to which those duties refer include in particular-
 - the provision and maintenance of systems of work, plant and machinery that, as far as is reasonably practicable, are safe and without risks to health;
 - taking such steps as may be reasonably practicable to eliminate or mitigate any hazard or potential hazard to the safety or health of employees, before resorting to personal protective equipment;
 - making arrangements for ensuring, as far as is reasonably practicable, the safety and absence of risks to health in connection with the production, processing, use, handling, storage or transport of articles or substances;
 - establishing, as far as is reasonably practicable, what hazards to the health or safety of persons are attached to any work which is performed, any article or substance which is produced, processed, used, handled, stored or transported and any plant or machinery which is used in his business, and he shall, as far as is reasonably practicable, further establish what precautionary measures must be taken with respect to such work, article, substance, plant or machinery in order to protect the health and safety of persons, and he shall provide the necessary means to apply such precautionary measures;
 - providing such information, instructions, training and supervision as may be necessary to ensure, as far as is reasonably practicable, the health and safety at work of his employees;
 - as far as is reasonably practicable, not permitting any employee to do any work or to produce, process, use, handle, store or transport any article or substance or to operate any plant or machinery, unless the precautionary measures contemplated in paragraphs (b) and (d), or any other precautionary measures which may be prescribed, have been taken;
 - taking all necessary measures to ensure that requirements of this Act are complied with by every person in his employment or on premises under his control where plant or machinery is used;
 - enforcing such measures as may be necessary in the interest of health and safety;
 - ensuring that work is performed and that plant or machinery is used under the general supervision of a person trained to understand the hazards associated with it and who have the authority to ensure that precautionary measures taken by the employer are implemented; and
 - causing all employees to be informed regarding the scope of their authority as contemplated in section 37 (1) (b).

The Occupational Health and Safety Act aims to provide for the health and safety of persons at work and for the health and safety of persons in connection with the activities of persons at work and to establish an advisory council for occupational health and safety. Health & Safety on site is the responsibility of the contractor and the proponent. Although this is not the function of the ECO, it is a standard requirement for building construction and must be monitored and evaluated by a suitably qualified Health & Safety person. It will not form part of any environmental audit in the future.

8 OPERATIONAL/MAINTENANCE PHASE ENVIRONMENTAL MANAGEMENT REQUIREMENTS

The Operational/Maintenance Phase of this EMP refers to the day to day management activities that are required to ensure sustainability and the achievement of the principles and objectives of the development. The requirements are applicable to the proponent, any HOA that is put in place, all employees and all visitors to the property.

8.1 <u>STORMWATER MANAGEMENT</u>					
Management Statement/Outcome			Impacts & Risks Avoided		
To ensure management of stormwater during operation phase.			To prevent erosion due to stormwater impact.		
Management Actions					
a. No stormwater runoff should be allowed to concentrate onto open spaces and roadways downstream of the property.					
Method of monitoring implementation	Frequency of Monitoring	Responsible Party for implementing management action	Time period	Mechanism for monitoring Compliance	Programme for reporting on Compliance
Ensure soft landscaping	Ongoing	Developer / HOA	As required	Audit	Audit
<ul style="list-style-type: none"> Concentration of stormwater runoff will be minimised through the application of landscaping techniques, i.e. by creating grass lined swales, undulations and depressions, vegetation. 					

8.2 <u>BOTANICAL / LANDSCAPING / REHABILITATION</u>					
Management Statement/Outcome			Impacts & Risks Avoided		
To ensure that indigenous vegetation is encouraged within urban areas.			Ongoing spread of alien invasive species. Ensure protected species are taken into consideration.		
Management Actions					
a. Applicant must practice ongoing alien invasive management.					
Method of monitoring implementation	Frequency of Monitoring	Responsible Party for implementing	Time period	Mechanism for monitoring Compliance	Programme for reporting on Compliance

		management action			
Visual / photographic	Ongoing	Owner	As required	Audit	Audit
b. Retain and manage protected and indigenous vegetation.					
Method of monitoring implementation	Frequency of Monitoring	Responsible Party for implementing management action	Time period	Mechanism for monitoring Compliance	Programme for reporting on Compliance
Visual / photographic	Ongoing	Owner	As required	Audit	Audit
<ul style="list-style-type: none"> • Rehabilitate with appropriate indigenous vegetation to promote soft landscaping. • Replace vegetation if it dies off. 					

9 MONITORING, MAINTENANCE & VALIDITY OF EMPR

9.1 MONITORING

Monitoring is an important tool in determining the effectiveness of management actions by measuring changes in the environment. These could be in the form of fixed-point photography where an area is photographed on a regular / seasonal basis to ascertain changes, monitoring of a particular aspect such as landscape integrity parameters, recordings of animal movement from fixed point etc. The most important aspect of any monitoring programme is **consistency and continuity**. This will ensure a level of scientific accuracy to determine baselines / thresholds and measure changes / deviations, which then drive management reactions.

Any required monitoring reports must be made available to the competent authority as required.

The type and frequency of monitoring must include:

- During construction photographs must be taken from pre-identified fixed points and a comprehensive record maintained by the ECO;
- Incident Reports;
- Site meeting minutes.

9.2 MONITORING TIMEFRAMES SUMMARY

Table 4: Monitoring Timeframe Summary

MONITORING TIMEFRAMES		
Type	Frequency	Criteria
ECO visits	As per section 5.4	Site photographs / site diary
Record keeping	Monthly	Site photographs, method statements, site meeting minutes (if applicable)
	6-month post construction	Completion Statement
Auditing	One year post construction	Compliance with the EA, EMPr, municipal permits. Note that GA compliance is the responsibility of the BGCMA.

9.3 ENVIRONMENTAL AUDITS

A final construction phase Completion Statement must be submitted within six (6) months of completion of construction / site handover.

This Completion Statement must include the monitoring results as above, where applicable to construction.

An independent Environmental Audit must be undertaken one (1) year post construction.

9.4 AUDIT REPORTS FREQUENCIES AND FORMAT

The table below provides a summary of the timeframes for the various Audit Reports specified in the EA.

Table 5: Audit Reports Timeframe Summary

ENVIRONMENTAL AUDIT TIMEFRAMES		
Type	Frequency	Criteria
Construction Audit	One year post construction	Audit on operational aspects of the EA and EMPr
Future audits	Competent Authority to confirm	Compliance with the Environmental Regulations for Audits

In terms of the 2014 EIA Regulations, Audit Reports must be submitted to the registered Interested & Affected Parties within 7 days of submission to the competent authority.

In order to comply with the 2014 EIA Regulations, any audits must be undertaken using the following format:

Table 6: Environmental Audit Requirements

Appendix 7 of Regulation 326 of the 2014 EIA Regulations, as amended contains the required contents of an Environmental Audit Report. The checklist below serves as a summary of how these objectives & requirements were incorporated into this Audit Report.	
Objective	Description
The objective of the environmental audit report is to -	
(a) Report on – (i) the level of compliance with the conditions of the environmental authorisation and the EMPr, and where applicable, the closure plan; and (ii) the extent to which the avoidance, management and mitigation measures provided for in the EMPr, and where applicable, the closure plan achieve the objectives and outcomes of the EMPr, and closure plan.	
(b) Identify and assess any new impacts and risks as a result of undertaking the activity.	
(c) Evaluate the effectiveness of the EMPr, and where applicable, the closure plan.	
(d) Identify shortcomings in the EMPr, and where applicable, the closure plan.	
(e) Identify the need for any changes to the avoidance, management and mitigation measures provided for in the EMPr, and where applicable, the closure plan.	
Requirement	Description
(1) An Environmental audit report prepared in terms of these Regulations must contain -	
(a) Details of – (i) The independent person who prepared the environmental audit report; and	

Appendix 7 of Regulation 326 of the 2014 EIA Regulations, as amended contains the required contents of an Environmental Audit Report. The checklist below serves as a summary of how these objectives & requirements were incorporated into this Audit Report.

Objective	Description
(ii) The expertise of independent person that compiled the environmental audit report.	
(b) A declaration that the independent auditor is independent in a form as may be specified by the competent authority.	
(c) An indication of the scope of, and the purpose for which, the environmental audit report was prepared.	
(d) A description of the methodology adopted in preparing the environmental audit report.	
(e) An indication of the ability of the EMPr, and where applicable the closure plan to – <ul style="list-style-type: none"> <li data-bbox="320 801 839 958">(i) Sufficiently provide for the avoidance, management and mitigation of environmental impacts associated with the undertaking of the activity on an on-going basis; <li data-bbox="320 969 839 1093">(ii) Sufficiently provide for the avoidance, management and mitigation of environmental impacts associated with the closure of the facility; and <li data-bbox="320 1104 839 1193">(iii) Ensure compliance with the provisions of environmental authorisation, EMPr, and where applicable, the closure plan. 	
(f) A description of any assumptions made, and any uncertainties or gaps in knowledge.	
(g) A description of an consultation process that was undertaken during the course of carrying out the environmental audit report.	
(h) A summary and copies of any comments that were received during any consultation process.	
(i) Any other information requested by the competent authority.	

Any other requirements of the EA or any other authorisations must be incorporated into an Audit where necessary.

10 DECOMMISSIONING PHASE ENVIRONMENTAL MANAGEMENT REQUIREMENTS

It is not likely that decommissioning of this facility will take place in the near future. However, in the event that decommissioning does occur, all relevant legislation and policies must be complied with for the given period.

In general, in the future event that the facility be decommissioned, the following must be undertaken:

- Demolition of buildings and removal of rubble must be undertaken without impacting on areas outside of the development area.
- Rubble must be disposed of correctly and to a registered site if not reused on site.
- Decommissioning must comply with any relevant legislation valid at that time.

11 NON-COMPLIANCE

Any person is liable on conviction of an offence in terms of regulation 49(a) of the National Environmental Laws Second Amendment Act (Act 30 of 2013) to imprisonment for a period not exceeding ten (10) years or to a fine not exceeding R10 million or an amount prescribed in terms of the Adjustment of Fines Act, 1991 (Act No. 101 of 1991).

It is the responsibility of the ECO to report matters of non-compliance to the Employer's Representative or the Holder of the EA if no representative is in place. It is the responsibility of the Holder of the EA, and not the ECO, to report such matters of non-compliance to the competent Authority.

11.1 PROCEDURES

The Holder of the EA shall comply with the environmental specifications and requirements of this EMPr, any Approval / License issued and Section 28 of NEMA, on an on-going basis and any failure on his part to do so will entitle the authorities to **impose a penalty**¹.

In the event of non-compliance the following recommended process shall be followed:

- The competent authority shall issue a **Notice of Non-compliance** to the Holder of the EA, stating the nature and magnitude of the contravention.
- The Holder of the EA shall **act to correct the transgression** within the period specified in by the authority.
- The Holder of the EA shall provide the competent authority with a **written statement** describing the actions to be taken to discontinue the non-conformance, the actions taken to mitigate its effects and the expected results of the actions.
- In the case of the Holder of the EA failing to remedy the situation within the predetermined time frame, the competent authority may recommend halting the activity.
- In the case of non-compliance giving rise to physical environmental damage or destruction, the competent authority shall be entitled to undertake or to cause to be undertaken such **remedial works** as may be required to make good such damage at the cost of the Project applicant.
- In the event of a dispute, difference of opinion, etc. between any parties in regard to or arising out of interpretation of the conditions of the EMPr, disagreement regarding the implementation or method of implementation of conditions of the EMPr, etc. any party shall be entitled to require that the issue be referred to **specialists and / or the competent authority** for determination.
- The competent authority shall at all times have the right to **stop work** and/or certain activities on site in the case of non-compliance or failure to implement remediation measures.

¹ A penalty may not necessarily be a monetary fine but could also be a stoppage in work time, additional mechanisms to prevent pollution or degradation at the cost of the proponent or even a directive to cease activities from the competent authority.

12 REFERENCES

Aquanotion, 2008. www.twoflush.com/conservbody.htm. Aquanotion Ltd, Alberta, Canada.

Eartheasy, 2008. www.eartheasy.com - Solutions for Sustainable Living.

eHow Home, 2011. www.eHow.com - *How to Safely Dispose of Energy Efficient Light Bulbs*.

Lochner, P. 2005. *Guideline for Environmental Management Plans*. CSIR Report No ENV-S-C 2005-053H, Republic of South Africa, Provincial Government of the Western Cape, Department of Environmental Affairs and Development Planning, Cape Town.
